# 2022 BOND PROJECTS – BOARD UPDATE

# Valley Oaks Elementary School

Spring Branch Independent School District SBISD Project No. 67303 PBK Project No. 220233 December 31, 2022

#### 1) PROJECT TEAM:

Owner:	Spring Branch ISD	Assoc. Superintendent for Ops: Project Manager:	Travis Stanford Geoff Bay
Architect:	PBK	Partner-in-Charge:	Brandon Ross
		Architect / Client Executive:	Philip Stewart
		Project Manager:	Gloria Carlos
CM @ Pick	Durotech Inc		

CM @ Risk: Durotech, Inc.

#### 2) GENERAL SCOPE OF WORK:

 Classroom additions, Dining Commons expansion and parking spaces extension while maintaining school operations during construction.

#### 3) BOND PLAN PROJECT TIMELINE:

 The following project is included in year one of the 2022 bond program. The Project Advisory Team is involved from the Schematic Design (SD) to the Design Development (DD) phase.

SCHEMATIC DEVELOPMENT	JULY 2022 – SEPTEMBER 2022	
DESIGN DEVELOPMENT	SEPTEMBER 2022 – NOVEMBER 2022	
CONSTRUCTION DOCUMENTS	NOVEMBER 2022 – FEBRUARY 2023	
ISSUE FOR PROPOSAL	FEBRUARY 2023 – MARCH 2023	
BIDDING / BOARD APPROVAL	MARCH 2023 – JULY 2023	
CONSTRUCTION PHASE	JULY 2023 – SEPTEMBER 2024	
CLOSEOUT	OCTOBER 2024	

# Current Point

### 4) **PROJECT STATUS OVERVIEW**:

- All PAT presentations are complete.
- Design Development phase has been completed.
- Construction Documents are in progress.

## 5) PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

The following activities have taken place:

• Project page-turn with facilities for 50% construction documents has been performed.

## 6) NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:


- Traffic Impact Analysis (TIA) Valley Oaks ES has been performed.
- PBK to submit 75% construction documents to SBISD and Durotech for review.

## 7) PHOTOGRAPHS:








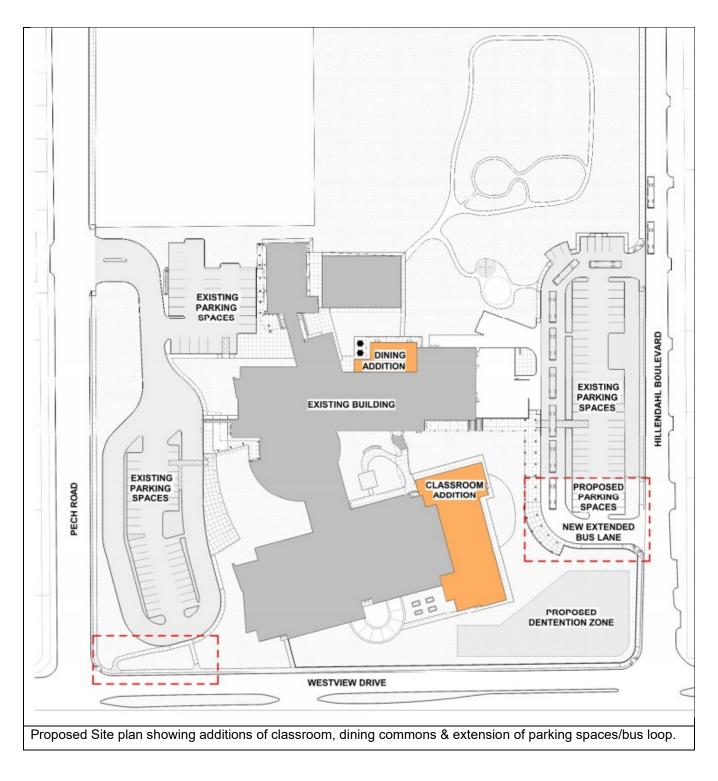



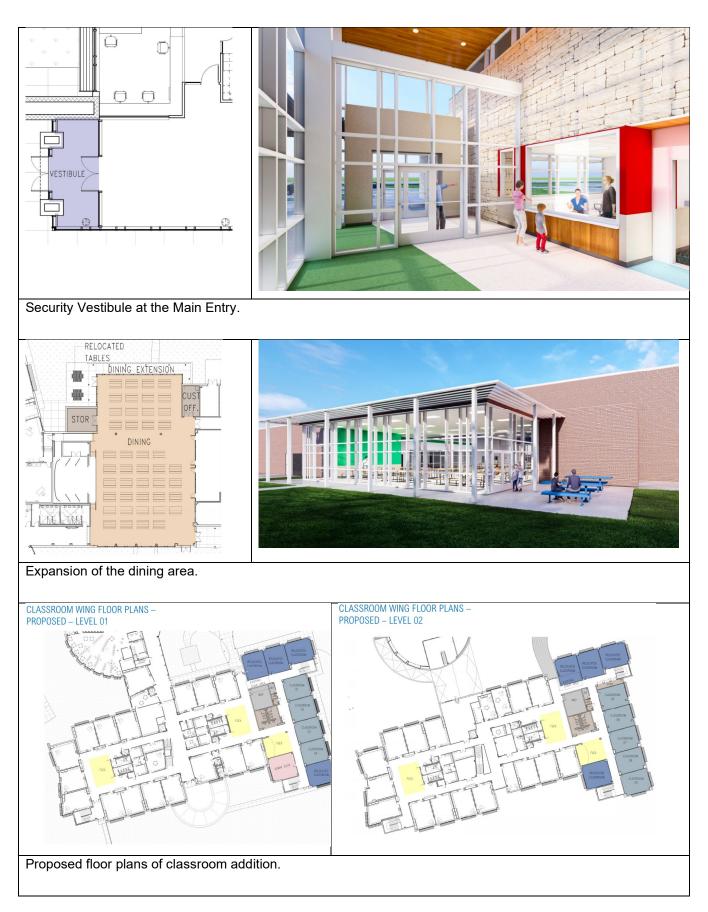





Proposed elevations of classroom addition.



Proposed elevations of classroom addition.
