

## 2017 BOND PROJECTS – BOARD UPDATE

# Stratford High School Addition and Renovations

Spring Branch Independent School District SBISD Project No. 67220 PBK Project No. 18148 December 31, 2019



1) PROJECT TEAM:

Owner: Spring Branch ISD Assoc. Superintendent of Ops: Travis Stanford

Project Manager: Max Buja

Architect: PBK Principal-in-Charge: Brandon Ross

Project Manager: Philip Stewart

CM @ Risk: Satterfield & Pontikes Construction, Inc.

## 2) GENERAL SCOPE OF WORK:

Addition of a 1,000 seat auditorium to the existing school. Also included are a roof replacement, safety & security, site lighting and site improvements for the campus.

#### 3) BOND PLAN PROJECT TIMELINE:

 The following project is included in year one of the bond program. The Project Advisory Team is involved from the Schematic Design (SD) to the Design Development (DD) phase.

<b>←</b>	Current
	Point
	Point
	<b>←</b>

#### 4) PROJECT STATUS OVERVIEW

 A/E team is moving forward into the Construction Document phase. CM @ Risk has submitted phasing and logistical reports.

#### 5) PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

The following activities have taken place:

- Progress toward Construction Documents.
- A/E held multiple design coordination meeting and engaged in site visits.
- Phasing and logistical planning has commenced.



### 6) NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

- Construction Documents will continue to move forward.
- First round of permits will be submitted to the City of Houston.
- Logistical coordination between school and construction teams will commence.
- CM@R will continue to price the school using the latest documents from the A/E.

## 7) PHOTOGRAPHS:






Schematic Design of Exterior.





Schematic Design of Auditorium

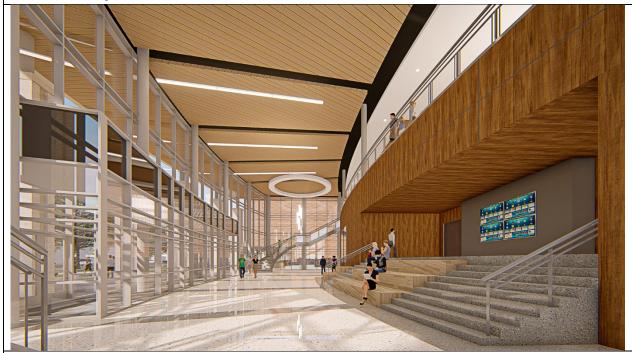

Schematic Design of Lobby





Schematic Design of a Collaboration Area
