

2022 BOND PROJECTS - BOARD UPDATE

Valley Oaks Elementary School

Spring Branch Independent School District SBISD Project No. 67303 PBK Project No. 220233 November 30, 2022



1) PROJECT TEAM:

Owner: Spring Branch ISD Assoc. Superintendent for Ops: Travis Stanford

Project Manager: Geoff Bay

Architect: PBK Partner-in-Charge: Brandon Ross

Architect / Client Executive: Philip Stewart

Project Manager: Gloria Carlos

CM @ Risk: Durotech, Inc.

2) GENERAL SCOPE OF WORK:

 Classroom additions, Dining Commons expansion and parking spaces extension while maintaining school operations during construction.

3) BOND PLAN PROJECT TIMELINE:

• The following project is included in year four of the bond program. The Project Advisory Team is involved from the Schematic Design (SD) to the Design Development (DD) phase.

SCHEMATIC DEVELOPMENT	JULY 2022 – SEPTEMBER 2022
DESIGN DEVELOPMENT	SEPTEMBER 2022 – NOVEMBER 2022
CONSTRUCTION DOCUMENTS	NOVEMBER 2022 – FEBRUARY 2023
ISSUE FOR PROPOSAL	FEBRUARY 2023 – MARCH 2023
BIDDING / BOARD APPROVAL	MARCH 2023 – JULY 2023
CONSTRUCTION PHASE	JULY 2023 – SEPTEMBER 2024
CLOSEOUT	OCTOBER 2024



4) PROJECT STATUS OVERVIEW:

- All PAT presentations are complete.
- Design Development phase has been completed.
- Construction Documents are in progress.

5) PAST 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:

The following activities have taken place:


- Surveying has been performed.
- Project has held PAT #03 and PAT #04.

6) NEXT 2-4 WEEKS PROJECT HIGHLIGHTS / MILESTONES:


- Traffic Impact Analysis (TIA) to be performed due to the additions to Valley Oaks ES.
- PBK to submit 50% construction documents to SBISD and Durotech for review.

7) PHOTOGRAPHS:



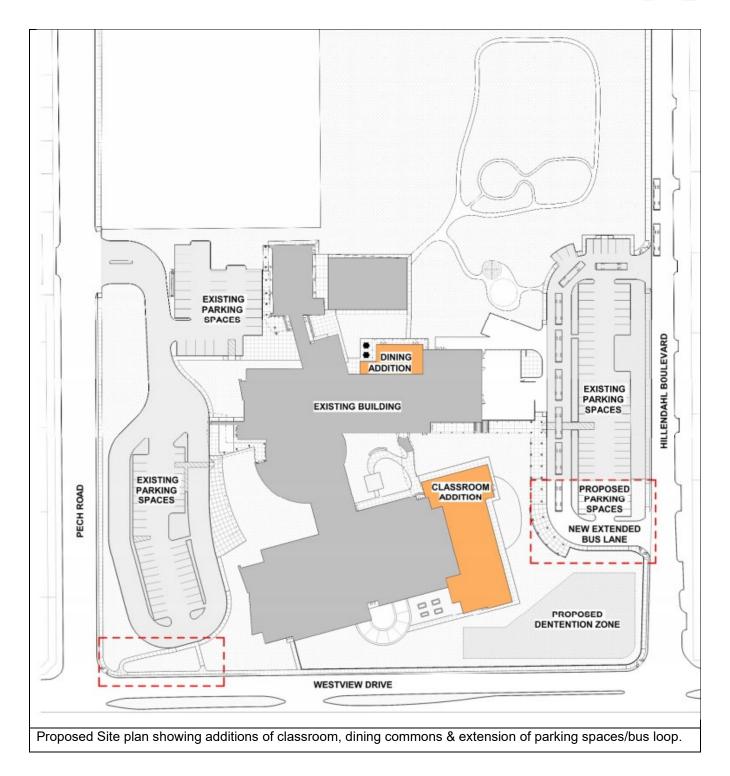




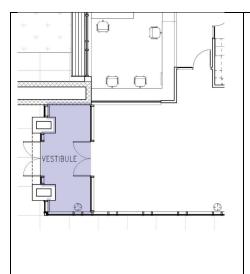



Security Vestibule at the Main Entry.





Expansion of the dining area.





Proposed floor plans of classroom addition.





Proposed elevations of classroom addition.



Proposed elevations of classroom addition.
