Great schools. Great community.



2017 Bond Program

Bond Oversight Committee (BOC)

February 6th, 2019

Agenda

- Introductions
 - Dr. Jennifer Blaine, Associate Superintendent for Talent and Operations/ Travis Stanford, Director of Planning & Construction
 - District Staff
 - BOC Committee Members
- BOC Charge
- Finance Updates
- Career & Technology Education (CTE) Updates
- Fine & Performing Arts Updates
- Technology Updates
- Transportation Updates
- Planning & Construction Updates
- BOC Discussions and Questions



District Staff

Dr. Scott Muri Superintendent

Dr. Jennifer Blaine Associate Superintendent for Talent and Operations

Karen Wilson Associate Superintendent for Finance

Linda Buchman Community Relations Officer

Christina Masick Chief Information Officer

Stephen Johnston Manager, Bond Projects

Dr. David Sablatura Director, CTE Department

Travis Stanford Director, Planning & Construction

BOC Co-Chairs

Lewis Gissel – Igissel3@gmail.com Kathy Goss – johngoss4@aol.com

BOC Charge

- Ensuring the bond projects remain faithful to the priorities identified in the 2017 Bond Plan approved by voters on November 7, 2017.
- Providing advice to the Board of Trustees on ways to maximize the potential of the 2017 Bond Plan and to provide the best value to the taxpayers of Spring Branch Independent School District.
- Reviewing and evaluating, on a quarterly basis, information from staff on all projects and expenditures of the bond funds on the timelines established in the 2017 Bond Plan.
- Working with staff in assessing key campus stakeholders' levels of satisfaction with the quality of work and rating of customer service (i.e. courtesy, knowledge and helpfulness of the bond project workers).
- Reviewing and evaluating, on a quarterly basis, a 2017 Bond Plan budget status report.
- Providing an annual report to the Board of Trustees on the progress of the 2017 Bond Plan.

 Great schools. Great community.

Meetings

The Bond Oversight Committee will hold a minimum of one meeting per quarter. At least a majority of the Committee members should be present to hold any scheduled meetings.



2017 Bond Plan

	Recommended	
Proposed Scope	Bond Plan	Remarks
8	g and the second	
FACILITIES	\$796,300,000	Facilities Scenario 7
	\$369,556,362	ES Transformation/Replacement
	\$287,229,965	MS + HS Addition/Renovation
	\$99,645,063	Building System Upgrades
	\$12,944,768	District Athletics (Includes 4 HS Turf Fields)
	\$26,923,842	Bond/Project Contingency
INSTRUCTION	\$13,000,000	SBISD Final Recommendation
	\$10,000,000	CTE: Refresh Existing Programming / Plan for future
	\$3,000,000	Fine Arts: Band Instruments + Uniforms
TECHNOLOGY	\$60,100,000	SBISD Final Recommendation
	\$18,728,000	Safety / Security Upgrades
	\$22,400,000	Network / Campus IT Infrastructure Modernization
	\$11,220,000	Staff Computer Life Cycle Management
	\$7,752,000	Student Devices Life Cycle Management
TRANSPORTATION	\$13,000,000	
		Replacement (73 Regular Buses)
		Replacement (8 Special Education Buses)
	4	
ADMINISTRATION	\$16,000,000	
		Bond Plan Administration
GRAND TOTAL	\$898,400,000	
SECURITARIA PARAMENTALISME		

Finance Updates:

Expenditures

Oct – Dec 2018 \$ 3,306,874
 July – Sept 2018 \$ 3,154,754

Inception through Dec 2018 \$ 8,626,085

Interest Earnings

Oct – Dec 2018 \$ 859,871

July – Sept 2018\$ 921,312

Inception through Dec 2018 \$ 1,879,250

Issuance

○ Issued June 2018 \$146,000,000

Authorized but not issued \$752,400,000

Career & Technology Education (CTE) Updates:

- The CTE Dept. has nearly completed its refresh of \$1.2 million of outdated technology in secondary CTE classrooms and labs across the District
- The CTE Task Force met six times in the fall of 2018 and completed the following work:
 - Conducting site visits to outstanding CTE programs in the area and State to review facilities, models for instructional delivery, and innovative programming
 - Creating a vision for a "world class" CTE program
 - Examining opportunities and challenges raised by stakeholders
 - Creating actionable recommendations to the Board for achieving the vision
- The CTE Task Force provided its vision and recommendations to the Board at the December 17 regular meeting. The Board provided feedback and guidance at the January 14 Board workshop, and directed administration to return to the Board with a roadmap and timeline for implementation.

Fine & Performing Arts Updates:

- Over \$2,000,000 in band and orchestra instruments have been ordered to date.
- High school drill team uniforms replacement cycles begin this school year.
- High school marching band uniform replacements scheduled to begin in 2021.
- Auditorium curtains are currently scheduled for replacement in 2025.



Memorial HS Band



Stratford HS Marching Band



Technology Updates:

- Four Major Project Areas
 - Lifecycle Refresh
 - Safety and Security
 - Network and Infrastructure Lifecycle Replacements
 - Technology





Technology Updates:

Lifecycle Refresh

- Student Devices
 - Secondary
 - Rollout schedule to December 2018 Board
 - Elementary
 - Provide allotment to campus based on age of existing student devices and enrollment February 2019
 - Consultative process to fit needs of campus
 - Order devices for next school year Spring 2019
- Adult Devices
 - Instructional Started January 2019
 - Replace computers as they are received for repair
 - Replace computers when new teachers enter the district
 - Staff
 - Proactive replacement of computers as the age out (5 years) Started January 2019



Technology Updates:

Safety and Security

- Network Security Equipment
 - Security Information & Event Management (SIEM)
 - Research & Tech Assessment Completed Summer 2018
 - Proof of Concept
 - Completed Fall 2018
 - Resulting in a different strategy and another POC solution
 - Installation On track to begin Spring 2019
- Security Camera Modernization
 - Camera Assessment Completed Fall 2018
 - Develop camera replacement and coverage strategy
- Wifi Equipment
 - Add hardware to data center for increased performance Spring 2019
 - Installed January 2019 and on track to cut over March 2019



Technology Updates:

Safety and Security (continued)

- Extended Network Availability
 - Research Completed Fall 2018
 - Finalizing contracts for work to begin in Spring 2019



Technology Updates:

Infrastructure

- Server Lifecycle Refresh
 - Data Center
 - Beginning procurement processes for remaining equipment Spring 2019
 - Scheduled implementation Summer 2019
- Cabling
 - Modernizing connections (fiber) between MDF and IDFs at non-replacement campuses
 - Completed issuance of RFP (December 2018) and currently evaluating RFP Responses (February 2019)
 - Work to begin Summer 2019
- Switches (Layer 2)
 - Replacing 20 year old switches
 - Completed issuance of RFP (December 2018) and currently evaluating RFP Responses (February)
 - Work to being Summer 2019



Technology Updates:

Infrastructure (continued)

- UPS Replacement
 - Replacing and adding UPS in IDF closets
 - Completed issuance of RFP (December 2018) and currently evaluating RFP Responses (February 2019)
 - Work to being Summer 2019

Technology Updates:

Other Technology Projects

- Time Collection Devices
 - Detailed Deployment Planning in progress
 - Pilot with Finance, HR, Technology Begin March 2019
 - District wide implementation projected completion Begin Fall 2019
 - 150 Clocks Across District
 - Multiple Clock-In Options Time Clock, Computer, Phone

Technology Updates:

Digital Expansions Completed

- Completed Phase 1 expansions 2018 Fall semester
 - MHS and SWHS
 - AOC, SBMS, SHS and NBHS
- Included school wide, grade level and/or programmatic deployments
- Completed Readiness Rubric





Technology Updates:

SY2018-19 Annual Home Access Survey Results by School **Question**: Does your child have access to the internet at home?

Elementary Schools

(Yes) % with Access to the Internet												
Elementary Schools	2018											
Buffalo Creek Elem	90%											
Bunker Hill Elem	98%											
Cedar Brook Elem	86%											
Edgewood Elem	87%											
Frostwood Elem	99%											
Hollibrook Elem	79%											
Housman Elem	88%											
Hunters Creek Elem	98%											
Meadow Wood Elem	97%											
Memorial Drive Elem	98%											
Nottingham Elem	98%											
Pine Shadows Elem	88%											
Ridgecrest Elem	88%											

(Yes) % with Acce	ss to the Internet
Elementary Schools	2018
Rummel Creek Elem	99%
SBAI Elem	100%
Shadow Oaks Elem	89%
Sherwood Elem	89%
Spring Branch Elem	84%
Spring Shadows Elem	84%
Terrace Elem	94%
Thornwood Elem	91%
Treasure Forest Elem	77%
Valley Oaks Elem	100%
Westwood Elem	84%
Wilchester Elem	99%
Woodview Elem	92%



Technology Updates:

SY2018-19 Annual Home Access Survey Results by School **Question**: Does your child have access to the internet at home?

Middle Schools

(Yes) % with Access to the Internet											
Middle Schools 2018											
Academy of Choice MS	82%										
Cornerstone Academy	99%										
KIPP	91%										
Landrum MS	87%										
Memorial MS	99%										
Northbrook MS	86%										
SBAI MS	100%										
Spring Branch MS	97%										
Spring Forest MS	97%										
Spring Oaks MS	91%										
Spring Woods MS	89%										
WAIS	96%										
YES Prep MS	91%										


High Schools

(Yes) % with Access to the Internet									
High Schools	2018								
Academy of Choice	91%								
Memorial High	99%								
Northbrook High	89%								
SBAI HS	100%								
Spring Woods High	91%								
Stratford High	99%								
WAIS HS	95%								
Yes Prep High	88%								

Technology Updates:




Technology Updates:

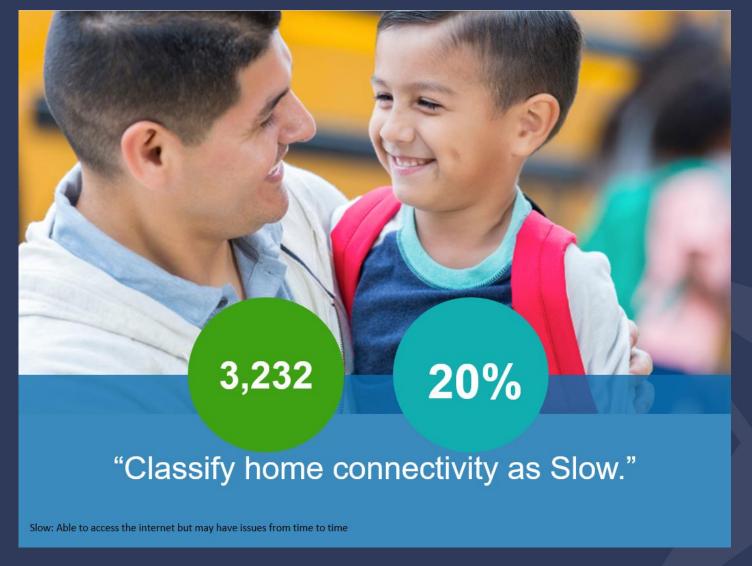

Technology Updates:

Options To Extend SBISD Network Availability

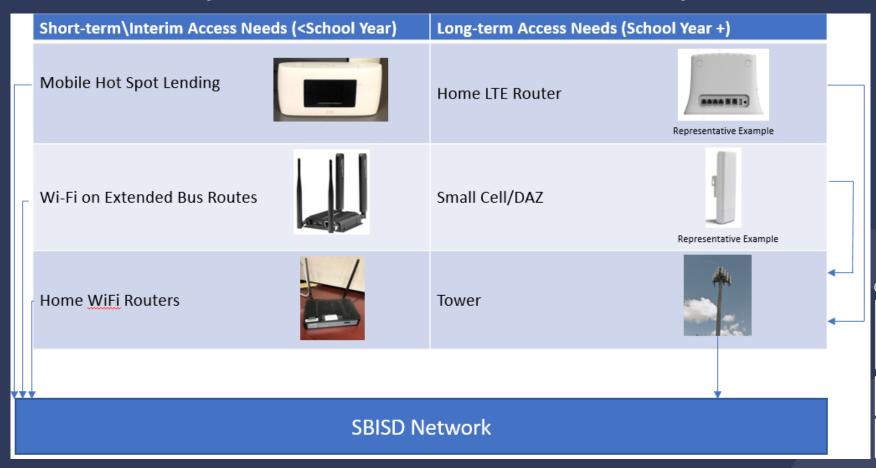

Technology Updates:

Scaling Digital Expansion at Secondary Campuses Launch Schedule through SY2019-20

Spring Semester 2019	Fall Semester 2019	Spring Semester 2020
Landrum MS\KIPP	Stratford HS	Cornerstone Academy
	Northbrook HS\YES Prep	Spring Branch MS (8 th)
	WAIS (HS & MS)	
	Memorial MS	
	Spring Forest MS	
	Spring Oaks MS	

NOTE: Campus specifics pending detailed campus-level planning and logistics



Transportation Updates:

• 25 buses will be ordered in the 2018/2019 school year.

SCHOOL YEAR	# OF BUSES SCHEDULED TO REPLACE	ADDITIONAL REG ED BUSES REQURIED FOR CAPACITY	# OF BUSES	REPLACEMENT AGE	ESTIMATED COST
2017/2018	0	0	0		0
2018/2019	19	6	25	15-17 yrs.	Less = \$521,477.00 (Grant Monies) = \$2,449,823.00
2019/2020	0	0	0		0
2020/2021	0	0	0		0
2021/2022	7	4	П	I5 yrs.	\$1,477,520.00
2022/2023	7	4	П	I 6 yrs.	\$1,443,365.00
2023/2024	8	3	П	17 yrs.	\$1,443,365.00
2024/2025	8	3	П	18 yrs.	\$1,443,365.00
2025/2026	8	3	П	17 yrs.	\$1,477,520.00
2026/2027	8	3	П	18 yrs.	\$1,511,675.00
Total	65	26	91		\$11,246,633.00

Revised Bus Replacement Schedule (2 Grants Received)

Planning & Construction Updates:

School: Pre-K Centers, Bear Blvd & Lion Lane

Scope of Work: Chiller Replacement & Courtyard Lighting Project

Project Manager: Kris Drosche

Architect/Engineer: Johnston, LLC - Contractor: Bass Construction

Status:



Scope/Update: Project in Warranty Phase. Project included new chillers for redundancy and new courtyard lighting. Controls and sensors were replaced by JCI during winter break.



BOND

2017
Spring Branch ISD

New Chiller Installed

Current Status

Planning & Construction Updates:

School: Pre-K Centers, Tiger Trail & Wildcat Way

Scope of Work: Chiller Replacement & Courtyard Lighting Project

Project Manager: Kris Drosche

Architect/Engineer: Johnston, LLC - Contractor: TBD

Yε	ear	1	(2	018	8)							Yε	ar	2	(2	019	9)						
J	F	М	Α	М	J	J	Α	S	0	Z	D	J	F	М	Α	М	J	٦	Α	S	0	Ν	D
Г						D	esię	gn			Proc	cure			Bld	g. S	yst	em	s				

1.4	ta	т	П	C
(e	La	ш		~ 1

PROJECT ADVISORY TEAM	NA
CMAR SELECTION	NA
SCHEMATIC DESIGN	NA
DESIGN DEVELOPMENT	NA
CONSTRUCTION DOCUMENTS	NOVEMBER 2018 – DECEMEMBER 2018
PERMIT RECEIVED	DECEMBER 2018 – JANUARY 2019
BIDDING / BOARD APPROVAL	FEBRUARY 2019 – MARCH 2019
CONSTRUCTION PHASE	MAY 2019 - AUGUST 2019
OCCUPANCY	AUGUST 2019

PROJECT STATUS OVERVIEW

Project has completed design and ready for permit review. Drawings have been sent to the City of Houston. Contractor pre-proposal on January 15th. Construction is set to begin in Summer 2019.



Planning & Construction Updates:

School: Pre-K Centers, Tiger Trail & Wildcat Way (continued)

Scope/Update: Replacement of existing chillers with larger capacity to add redundancy to HVAC chilled water at both campuses. Also, installation of new LED lighting in school's courtyard.

PROJECT HIGHLIGHTS / MILESTONES:

- Request for proposals for contractors
- Pre-proposal conference on January 15, 2019
- CSP recommendation set for March 2019 Board Meeting



The Widest Way School and Louis to fast Laurency and Louis to fast Laurency

The Tiger Trail School

The Wildcat Way School



Planning & Construction Updates:

Buffalo Creek ES

Scope of Work: Renovation Project

Project Manager: Matisia Hollingsworth

Architect/Engineer: Huckabee & Associates, Inc. - **Contractor**: TBD

Υe	e	ar	1	(2	0:	18	3)							Υe	ear	2	(2	019	— 9)							Υe	ear	3	(2	020) (C						
J		F	М	Α	N	Л	J	J	Α	s	0	N	D	J	F	М	Α	М	J	J	Α	s	0	N	D	J	F	М	Α	М	J	J	Α	S	o	N	D
					_	İ			D	esi	gn				। Pro	cure	2			I	l lajo	r R	enc	vat	ion	s (14 ı	no:	s)			Oc	cup	ľ			

Status:

PROJECT ADVISORY TEAM	SEPTEMBER 2018 – DECEMBER 2018
CONTRACTOR SELECTION	JANUARY 2019 – MARCH 2019
SCHEMATIC DESIGN	MAY 2018 – SEPTEMBER 2018
DESIGN DEVELOPMENT	AUGUST 2018 – OCTOBER 2018
CONSTRUCTION DOCUMENTS	OCTOBER 2018 – DECEMBER 2018
BIDDING / BOARD APPROVAL	JANUARY/2019 – MARCH 2019 ◀
PERMIT RECEIVED	MAY 2019
CONSTRUCTION PHASE	MAY 2019 – JUNE 2020
OCCUPANCY	AUGUST 2020

Current Status

PROJECT STATUS OVERVIEW

Facility walk-throughs of the campus and roof have been held with SBISD Facilities and Maintenance
Departments and Huckabee. Multiple Fact-Finding Meetings were held on campus with BCE Principal,
Staff & Huckabee. Four Project Advisory Team Introductory Meetings were held from September 2018 – November 2018

Planning & Construction Updates:

School: Buffalo Creek ES (continued)

Scope/Update: Project to include roof replacement and major interior renovations to restrooms, library and to the four collaboration areas and installation of Active Walls in all classrooms. Project to be bid Spring of 2019 and construction to begin Summer of 2019.

PROJECT HIGHLIGHTS / MILESTONES:

- Project issued for bidding on December 19, 2018.
- Project submitted to City of Houston for permitting in December 2018.
- Pre-Proposal Meeting on January 16, 2019
- CSP recommendation set for March 2019 Board Meeting



Buffalo Creek ES PAT Meeting



Planning & Construction Updates:

School: Cedar Brook ES

Scope of Work: Renovation Project and Classroom Addition

Project Manager: Matisia Hollingsworth

Architect/Engineer: Huckabee & Associates, Inc. - Contractor: TBD

	, ,													·																								
Ye	ea	ar	2	(:	2()1	9)								Ye	ear	. 3	(2	02	D)							Υe	ear	4	(2	02:	1)						
J		F	М	1	A	М	J		J	Α	S	0	Ν	D	J	F	М	Α	М	J	J	Α	S	0	Ν	D	J	F	М	Α	М	J	J	Α	S	0	N	D
Е		Design Procure									Major Renov. + Addition (14 Clrm A										۱dd	itio	n) 1	l8 r	nos		Oc	cup	у									

Status:

PROJECT ADVISORY TEAM	JANUARY 2019 – MAY 2019
CONTRACTOR SELECTION	JANUARY 2019 – MARCH 2019
SCHEMATIC DESIGN	JANUARY 2019 – APRIL 2019
DESIGN DEVELOPMENT	APRIL 2019 – JUNE 2019
CONSTRUCTION DOCUMENTS	JUNE 2019 – AUGUST 2019
BIDDING / BOARD APPROVAL	AUGUST 2019 – SEPTEMBER 2019
PERMIT RECEIVED	OCTOBER 2019
CONSTRUCTION PHASE	OCTOBER 2019 – JULY 2021
OCCUPANCY	SEPTEMBER 2021

Current Status

PROJECT STATUS OVERVIEW

Multiple Fact-Finding Meetings were held on campus with CBE Principal, Staff and Huckabee. Proposed scope of work to include interior and exterior renovations and new classroom wing addition.

Planning & Construction Updates:

School: Cedar Brook ES (continued)

Scope/Update: New classroom wing addition and interior and exterior renovations of existing campus. The project to include repairs of the existing roofing system including the replacement of the standing seam metal roof, mechanical system upgrades, Library renovations and replacement of skylight panels and providing new clearstory windows and renovation at the Collaboration spaces, replacement of door hardware at classrooms, fire alarm system replacement, security alarm and access control improvements and renovation of existing restrooms.

PROJECT HIGHLIGHTS / MILESTONES:

- PAT Meeting one on January 15th, 2019
- CMAR recommendation set for March 2019 Board Meeting







Planning & Construction Updates:

School: Hunters Creek ES

Scope of Work: New Construction/Replacement Campus

Project Manager: Kris Drosche, Noel Moreno & Travis Stanford

Architect/Engineer: Pfluger Associates, L.P. - **Contractor**: TBD

Year 2 (2019)	Year 3 (2020)	Year 4 (2021)
J F M A M J J A S O N D	J F M A M J J A S O N D	J F M A M J J A S O N D
Design Procure	ES Replacement (Off-Site: STC Trans	sition) 18 mos Occupy

SCHEMATIC DESIGN	MARCH 2019 – APRIL 2019
PROJECT ADVISORY TEAM	JANUARY 2019 – NOVEMBER 2019
CMAR SELECTION	JANUARY 2019 – FEBRUARY 2019
SCHEMATIC DESIGN	MARCH 2019 – APRIL 2019
DESIGN DEVELOPMENT	MAY 2019 – AUGUST 2019
CONSTRUCTION DOCUMENTS	SEPTEMBER 2019 – DECEMBER 2019
PERMIT RECEIVED	JANUARY 2020 – FEBRUARY 2020
BIDDING / BOARD APPROVAL	JANUARY 2020 – MARCH 2020
CONSTRUCTION PHASE	APRIL 2020 – JULY 2021
OCCUPANCY	AUGUST 2021

Current Status

PROJECT STATUS OVERVIEW

Multiple Fact-Finding Meetings were held on campus with HCE Principal, Staff and Plfuger. PAT Meetings are in process. The PAT Meetings are currently in the Programming/Conceptual Design Phase.

Planning & Construction Updates:

School: Hunters Creek ES (continued)

Scope/Update: Hunters Creek ES will be one of nine replacement elementary schools in the 2017 bond. The students will be relocated to the south transition campus during the rebuilding process.

PROJECT HIGHLIGHTS / MILESTONES:

CMAR recommendation set for March 2019 Board Meeting





Hunters Creek ES PAT Meeting


Planning & Construction Updates:

School: Treasure Forest ES

Scope of Work: Renovation Project

Project Manager: Matisia Hollingsworth

Architect/Engineer: Huckabee & Associates, Inc. - **Contractor**: TBD



Status:

PROJECT ADVISORY TEAM	SEPTEMBER/2018 – DECEMBER/2018
CONTRACTOR SELECTION	JANUARY/2019 – MARCH/2019
SCHEMATIC DESIGN	MAY/2018 – SEPTEMBER/2018
DESIGN DEVELOPMENT	AUGUST/2018 – OCTOBER/2018
CONSTRUCTION DOCUMENTS	OCTOBER/2018 – DECEMBER/2019
BIDDING / BOARD APPROVAL	JANUARY/2019 – MARCH 2019
PERMIT RECEIVED	MAY 2019
CONSTRUCTION PHASE	MAY/2019 – JUNE 2020
OCCUPANCY	AUGUST 2020

Current Status

PROJECT STATUS OVERVIEW

Facility walk-throughs of the campus and roof have been held with SBISD Facilities and Maintenance Departments and Huckabee. Multiple Fact-Finding Meetings were held on campus with TFE Principal, Staff & Huckabee. Four Project Advisory Team Meetings were held from September 2018 – November 2018.

Planning & Construction Updates:

School: Treasure Forest ES (continued)

Scope/Update: Project to include roof replacement and major interior renovations to restrooms, library and to the four collaboration areas and installation of Active Walls in all classrooms. Project to be bid Spring of 2019 and construction to begin Summer of 2019.

PROJECT HIGHLIGHTS / MILESTONES:

- Project issued for bidding on December 19, 2018.
- Project submitted to City of Houston for permitting in December 2018.
- A Pre-Proposal Meeting on January 16, 2019
- CSP recommendation set for March 2019 Board Meeting



Treasure Forest ES PAT Meeting



Planning & Construction Updates:

School: Landrum MS

Scope of Work: New Construction/Replacement Campus

Project Manager: Kris Drosche & Travis Stanford

Architect/Engineer: Stantec Architects - **Contractor**: TBD

Y	e	ar	2	(2	01	9)							Υє	ear	· 3	(2	02	— 0)							Υє	ear	4	(2	02:	 1)						
J		F	М	Α	М	J	J	Α	S	0	Z	D	J	F	М	Α	М	J	J	Α	S	0	Z	D	J	F	М	Α	М	J	J	Α	S	o	Ν	D
	Design Procure										N	/IS I	Rep	lace	emo	ent	(Of	f-Si	te:	ET	C)	18	mo	S			Oc	cup								

Status:

JANUARY 2019 – NOVEMBER 2019
JANUARY 2019 – MARCH 2019
AUGUST 2018 – DECEMBER 2018
JANUARY 2019 – MARCH 2019
MARCH 2019 – MAY 2019
MAY 2019 - AUGUST 2019
SEPTEMBER 2019 – NOVEMBER 2019
AUGUST 2019 – NOVEMBER 2019
JANUARY 2020 – DECEMBER 2021
JUNE 2021 – AUGUST 2021

Current Status

PROJECT STATUS OVERVIEW

Conceptual Site Studies have been completed to determine potential site impacts on both the construction and transition opportunities available at the existing campus. Studies have indicated that a 3 story on site rebuild is feasible.

Planning & Construction Updates:

School: Landrum MS (continued)

Scope/Update: Landrum MS will be replaced in the 2017 bond. The replacement school will be a three story building. The students will remain in the current building during the replacement process.

PROJECT HIGHLIGHTS / MILESTONES:

- Official design phase of the project will begin in January.
- CMAR recommendation set for April 2019 Board Meeting





Planning & Construction Updates:

School: Spring Oaks MS

Scope of Work: Renovation Project

Project Manager: Noel Moreno

Architect/Engineer: Pfluger Associates, L.P. - **Contractor**: TBD



Status:

SITE WALK	JULY/2018 – SEPTEMBER/2018
SCHEMATIC DESIGN	AUGUST/2018 – SEPTEMBER/2018
100% DESIGN DEVELOPMENT	SEPTEMBER/2018 – OCTOBER/2018
50% CONSTRUCTION DOCUMENTS	OCTOBER/2018 – NOVEMBER/2018
100% CONSTRUCTION DOCUMENTS	NOVEMBER 2018 – DECEMBER/2018
BIDDING / BOARD APPROVAL	FEBRUARY/2019 – APRIL/2019 -
PERMIT RECEIVED	FEBRUARY/2019 – APRIL/2019
CONSTRUCTION PHASE	MAY/2019 – MARCH/2020
TEMPORARY OCCUPANCY	JULY/2019 – AUGUST/2019
SUBSTANTIAL COMPLETION	APRIL/2020

Current Status

PROJECT STATUS OVERVIEW

The project is currently in the Bidding Phase.

Planning & Construction Updates:

School: Spring Oaks MS (continued)

Scope/Update: The project includes major roof replacement. The clinic and front office will be relocated and renovated to improve safety and security. Project to be bid Spring of 2019 and construction to begin Summer of 2019.

PROJECT HIGHLIGHTS / MILESTONES:

- Bidding phase
- Pre Proposal conference on January 15, 2019
- CSP recommendation set for March 2019 Board Meeting





Spring Oaks MS

Planning & Construction Updates:

School: Memorial HS

Scope of Work: Development of Campus Master Plan

Project Manager: Kris Drosche & Travis Stanford

Architect/Engineer: Stantec Architects - **Contractor**: TBD

Year 1 (2018) Year 2 (2019) Year 3 (20	020) Year 4 (2021)	Year 5 (2022)
J F M A M J J A S O N D J F M	M J J A S O N D J F M A	M J J A S O N D J F M A M J J A S O N D	J F M A M J J A S O N D
Master Plan	Bldg. Design Procure-2	Partial Rebuild: Phase 1 (On-Site: 24 months)	Оссиру

	ıs:

DECEMBER 2018 – DECEMBER 2019
APRIL 2018 – JULY 2018
AUGUST 2018 – DECEMBER 2018
JANUARY – MARCH 2019
APRIL – JUNE 2019
JULY – NOVEMBER 2019
TBD (APPROX. MARCH 2020)
EARLY 2020
APRIL 2020 – APRIL 2022
SUMMER 2022

Current Status

PROJECT STATUS OVERVIEW:

Completed all five Master Plan Advisory Team (MPAT) Meetings. The MPAT provided a clear on the Master Plan and the Board of Trustees voted unanimously to approve the the December 17th Board Meeting.



Planning & Construction Updates:

School: Memorial HS (continued)

Scope/Update: The scope of work is to first develop a Master Plan for MHS and identify Phase 1 of the Master Plan which will include replacing certain classroom buildings and the installation of a turf field. The Master Plan is to be recommended for approval at the December Board meeting.

PROJECT HIGHLIGHTS / MILESTONES:

- PAT Meetings dates
- Start the Schematic Design Phase
- CMAR recommendation set for April 2019 Board Meeting



Master Plan presented at December Board Meeting



Memorial HS MPAT Meeting

Current Status

Planning & Construction Updates:

School: Northbrook HS

Scope of Work: Renovation Project & Classroom Additions

Project Manager: Kris Drosche & Noel Moreno

Architect/Engineer: PBK Architects, Inc. - Contractor: TBD

Year 2 (2019)		Year 3 (2020)		Year 4 (2021)		
J F M A M J J A S O	N D	J F M A M J	J A S O N	D J F M A M J	J A S O N	D
Design	cure	18-Cla	Occupy			

4	-	IS:

PROJECT ADVISORY TEAM	MARCH 2019 – OCTOBER 2019
SCHEMATIC DESIGN	MARCH 2019 - MAY 2019
DESIGN DEVELOPMENT	MAY 2019 - AUGUST 2019
CMAR SELECTION	FEBRUARY 2019 - MARCH 2019
CONSTRUCTION DOCUMENTS	AUGUST 2019 – OCTOBER 2019
PERMIT RECEIVED	OCTOBER 2019 – DECEMBER 2019
BIDDING / BOARD APPROVAL	DECEMBER 2019 – FEBRUARY 2020
CONSTRUCTION PHASE	FEBRUARY 2020 – AUGUST 2021
OCCUPANCY	FEBRUARY 2020 – AUGUST 2021

PROJECT STATUS OVERVIEW

Initial Fact Finding Meetings have been held with the principal and staff in advance of the PAT Meetings. The CMAR process has been started for this project. The Design Team is conducting site surveys of the campus.



Planning & Construction Updates:

School: Northbrook HS (continued)

Scope/Update: The project will receive a classroom addition, major interior renovation, system upgrades, site work and a new artificial turf field.

PROJECT HIGHLIGHTS / MILESTONES:

- PAT Meeting dates
- CMAR recommendation set for April 2019 Board Meeting





Planning & Construction Updates:

School: Spring Woods HS

Scope of Work: Major MEP Upgrades, Renovations to Library and Cafeteria

Project Manager: Kris Drosche

Architect/Engineer: PBK Architects, Inc. - Contractor: TBD

Ye	ea	ar	1	(2	01	— 8)							Υe	ear	· 2	(2	01	9)							Υe	ear	. 3	(2	020	D)						
J		F	М	Α	М	J	J	Α	S	0	N	D	J	F	М	Α	М	J	J	Α	S	0	N	D	j	F	М	Α	М	J	J	Α	S	0	N	D
		*****						D	esi	gn				Pro	cure	9		L	.ibra	ary	+ C	afe	teri	a N	/lod	s (1	L4 n	105	;)		Oc	cup	1			

	_	
4	4	 ıc.
_		

PROJECT ADVISORY TEAM	AUGUST 2018 – DECEMBER 2018
CMAR SELECTION	NOVEMBER 2018 – FEBRUARY 2019
SCHEMATIC DESIGN	AUGUST 2018 - OCTOBER 2018
DESIGN DEVELOPMENT	OCTOBER 2018 – DECEMBER 2018
CONSTRUCTION DOCUMENTS	NOVEMBER 2018 – FEBRUARY 2019
PERMIT RECEIVED	FEBRUARY 2019 - MAY 2019
BIDDING / BOARD APPROVAL	FEBRUARY 2019 - MAY 2019
CONSTRUCTION PHASE	MAY 2019 - AUGUST 2020
OCCUPANCY	MAY 2019 - AUGUST 2020

Current Status

PROJECT STATUS OVERVIEW

PAT Meetings have been held and in these meetings the renovations for the cafeteria and library have been designed. Site surveys of the existing campus are being conducted.

Planning & Construction Updates:

School: Spring Woods HS (continued)

Scope/Update: The project will receive major mechanical renovations for better climate control and structural repairs. In addition, major renovations will occur to the cafeteria and library. Cafeteria will be expanded for additional seating and windows added. The library will receive a major reconfiguration to include new circulation desk, learning stairs and several large flexible spaces.

PROJECT HIGHLIGHTS / MILESTONES:

- Construction documents are continuing to be produced.
- CMAR to be selected for the project in the beginning of next year.
- Construction document reviews to be conducted with district personnel.
- CMAR recommendation set for February 2019 Board meeting



Spring Woods HS PAT Meeting



Planning & Construction Updates:

School: Stratford HS

Scope of Work: Renovation Project, Roof Replacement & New Auditorium

Project Manager: Kris Drosche & Travis Stanford

Architect/Engineer: PBK Architects, Inc. - **Contractor**: TBD

Ye	ea	ar	2	(2	01	9)							Υe	eai	3	(2	02	0)							Yε	ear	4	(2	02:	1)						
J		F	Μ	1	Α	Ν	1	J	J	Α	S	0	Z	D	J	F	М	Α	М	J	J	Α	S	0	Ν	D	J	F	М	Α	М	J	J	Α	S	0	N	D
							D	es	igr					Pro	cure	е	Auditorium Addition (16 mos)							Oc	cup	у	20000000											

ra	41	ıc

PROJECT ADVISORY TEAM	MARCH 2019 – SEPTEMBER 2019
SCHEMATIC DESIGN	MARCH 2019 - APRIL 2019
DESIGN DEVELOPMENT	APRIL 2019 – SEPTEMBER 2019
CMAR SELECTION	MAY 2019 - JUNE 2019
CONSTRUCTION DOCUMENTS	SEPTEMBER 2019 – DECEMBER 2019
PERMIT RECEIVED	DECEMBER 2019 – FEBRUARY 2020
BIDDING / BOARD APPROVAL	FEBRUARY 2020 - MARCH 2020
CONSTRUCTION PHASE	MARCH 2020 – AUGUST 2021
OCCUPANCY	MARCH 2020 - AUGUST 2021

PROJECT STATUS OVERVIEW

Initial fact finding meetings have been held with the principal and staff in advance of the PAT meetings that will begin in March. Design team is conducting site surveys of the campus

Current Status



Planning & Construction Updates:

School: Stratford HS (continued)

Scope/Update: The project will receive a new thousand seat auditorium, major interior renovation, system upgrades, new roof and a new artificial turf field.

PROJECT HIGHLIGHTS / MILESTONES:

- PAT Meeting dates
- CMAR recommendation set for May 2019 Board meeting



Stratford HS



Planning & Construction Updates:

PAT Meetings Schedule

	Meeting 1	Meeting 2	Meeting 3	Meeting 4	Meeting 5	Meeting 6	Meeting 7	Meeting 8
Cedar Brook ES	Tues. Jan. 15th, 2019 3:00-5:00 PM	Tues. Feb. 5th, 2019 3:00-5:00 PM	Tues. Feb. 26th, 2019 3:00-5:00 PM	Tues. March 19th, 2019 3:00-5:00 PM	Tues. April 16th, 2019 3:00-5:00 PM	Tues. May 7th, 2019 3:00-5:00 PM	Tues. Sept. 10th, 2019 3:00-5:00 PM (tentative)	
Hunters Creek ES	Wed. Jan. 23rd, 2019 3:15-4:45 PM	Wed. Jan. 30th, 2019 3:15-4:45 PM	Wed. Feb. 6th, 2019 3:15-4:45 PM	Wed. Feb. 20th, 2019 3:15-4:45 PM	Wed. March 20th, 2019 3:15-4:45 PM	Wed. May 15th, 2019 3:15-4:45 PM	Wed. Aug. 14th, 2019 3:15-4:45 PM (tentative)	Wed. Nov. 6th, 2019 3:15-4:45 PM (tentative)
Landrum MS	Tues. Jan.15th, 2019 4:00-5:30 PM	Mon. Jan. 28th, 2019 4:00-5:30 PM	Tues. Feb. 19th, 2019 4:00-5:30 PM	Tues. March 19th, 2019 4:00-5:30 PM	Tues. April 23rd, 2019 4:00-5:30 PM			
Memorial HS	Thurs. Jan. 24th, 2019 3:30-5:00 PM	Tues. Feb. 5th, 2019 3:30-5:00 PM	Wed. Feb. 27th, 2019 3:30-5:00 PM	Tues. April 9th, 2019 3:30-5:00 PM	Tues. May 14th, 2019 3:30-5:00 PM			
Northbrook HS	Meeting dates are in	development and are	proposed to begin	mid March 2019			Great schools.	Great community
Stratford HS	Meeting dates are in	development and are	proposed to begin	late February 2019			BC	
							20	D17
								Branch ISD

BOC Discussions and Questions



Thank You

The next BOC meeting will be held

May 1st, 2019

5:30 pm Dinner

6:00 pm Meeting

